Group 7 – Student Organization Event Registration & Attendance System

Project Plan

Version No: 1.00
Updated By: Talisic, Jhon Rosell
Approved By:

TÜVRheinland CERTIFIED
Management System ISO 9001:2015
www.tuv.com ID 9108636079

Revision History

Rev No.	MODIFIED BY	MODIFIED DATE	REMARKS	PRELIMINARY REVIEW & APPROVAL	DATE REVIEWED	FINAL REVIEW & APPROVAL	DATE APPROVED
1.00	Talisic, Jhon Rosell	2026/09/05	Initial Creation	Last Name, First Name	yyyy/mm/dd	Last Name, First Name	yyyy/mm/dd

PROJECT INTRODUCTION

Project Overview

GROUP NAME	Group 7
PROJECT NAME	Student Organization Event Registration & Attendance System
PROJECT CODE	
CLIENT	Alliance Software Inc.
BUSINESS UNIT	
ACCOUNT CATEGORY	☑ Single Project / App Account ☐ Multiple Project/App Account
PROJECT TYPES	☐ Prototype ☐ Production Support ☐ Enhancement / Request for Change (RFC) ☑ Ground Up ☐ Others
	If others, please specify:
	Note: For Multiple Enhancement/RFC and Ground Up, create a sub-Project Plan per Activity. For Production Support, refer to Project Monitoring Tool (ie. JIRA, Mantis, SugarCRM, Case Portal, Excel) for the Case Details.
PROCESS/ES FOLLOWED	☐ Production ☑ Agile/Iterative (For RFC & Ground Up) ☐ Waterfall ☐ Client Specific
HOLIDAY CALENDAR	☐ Client Holiday Calendar ☑ Alliance Cebu Holiday Calendar ☐ Alliance Manila Holiday Calendar
PROJECT DESCRIPTION	A basic web-based event registration and attendance system for student organizations. It allows officers to create and publish events, members to register online, and organizers to record attendance during the event. The system can also track certificate eligibility and generate participation reports for post-event evaluation.

Project Development Environment

Project Objectives

1. Programming Language
   - Front-end : Razor
   - Backend : Asp .Net Core & C#
2. IDE : Visual Studio
3. DB : SQL Server
4. Design Tools : Figma
5. 3rd Party Apps/Libraries :
6. Supported Browser
   - Chrome :
   - Firefox :
   - Safari :
   - Internet Explorer :
   - Microsoft Edge :
7. Supported Mobile Platforms
   - iOS :
   - Android :
   - Windows :
   - Mobile Responsive? :
8. Screen Resolution : 1920 x 1080 px
9. Server Information
   - Developer Server :
   - Staging / QA Server :
   - Production Server :
10. Mode of Access : ☐ Intranet ☐ Internet ☐ Both

Resource Capacity

Team Composition

- If Project is time & material- indicate monthly billed headcount
- If Project is Project-based - indicate total estimate breakdown

ACTIVE MEMBERS

YEAR: 2026

***Legend*: B** – *Billed*, **IB** – *Internal Billed*, **S** – *Support*

Role	Member	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
PROJECT MANAGER	Talisic, Jhon Rosell												
TECHNICAL MANAGER	Gabutan, Jerhon Clyde												
TECHNICAL LEAD	Singco, John Paul												
SA / DEV													
DEVELOPERS (#)	Gabutan, Jerhon Clyde												
	Pinca, Seth												
	Singco, John Paul												
	Taguiam, Jasper												
	Talisic, Jhon Rosell												
QA (#)	Taguiam, Jasper												
	Count Billed	1.00											
	Count Internal Buffer	1.00											
	Count Support	1.00											

Risk Management

Risk Analysis

Risk	Probability	Consequence	Prevention	Mitigation
Broad Feature Scope – key functions across Authentication (registration approval rules), Master Data (member/venue specs), Transactions (QR check-in & certificate logic), Reports, and Admin controls lack finalized edge-case details.	High	Extended project schedule and rework on backend database schemas and API routes.	Finalize and lock down the detailed functional requirements and wireframes for all five modules prior to active feature development.	Freeze the core MVP scope (Authentication, Event Creation, QR Check-In, Basic Reports) and defer non-essential features (e.g., certificate tracking) to a secondary backlog.
Power Interruption / Brownouts – sudden electrical loss or scheduled power interruptions in Metro Cebu disrupt local workstation setups and cause loss of uncommitted work.	High	Loss of unsaved dev work, halted local API development, and missed dev hours.	N/A	Enforce local offline development workflows, frequent Git commits, and render extra dev hours once grid power stabilizes.
Academic Schedule Conflicts – competing academic workloads, exam periods, and mandatory campus events limit team members' active dev hours.	High	Delayed task completions and missed milestone deadlines.	Review academic calendars prior to sprint planning and assign smaller, modular tasks during heavy exam weeks.	Reallocate pending tasks among available team members and adjust sprint delivery targets.
Integration & API Bugs – bugs and logic failures encountered during system module integration (e.g., API validation errors or broken scanner routes).	High	Unstable software builds and additional time spent debugging late in the cycle.	Enforce standard coding guidelines, conduct peer code reviews, and write basic test cases.	Prioritize critical bugs in a dedicated triage log, assign developers to resolve blockers, and perform regression testing.

Risk Analysis

Risk	Probability	Consequence	Prevention	Mitigation
Natural Disasters & Severe Weather – typhoons, flooding, or earthquakes during the Philippine "Ber" months (September–December) causing power loss and internet disruptions.	Mid	Interrupted project activities, unavailable team members, and severe schedule delays.	N/A	Shift project deadlines based on severity, enable asynchronous remote work once utilities recover, and restore latest code from cloud backups.
Network & Connectivity Outages – ISP service interruptions, fiber cuts, or mobile data instability prevent real-time team collaboration, remote repo pushes, and API endpoint testing.	Mid	Inability to push/pull code from remote repositories, interrupted virtual standups, and blocked cloud database connections.	N/A	Set up offline-first local development configurations, utilize mobile hotspots for critical commits, and shift to asynchronous task communication.
Poor Team Communication & Task Misalignment – lack of active updates, unclear task handoffs, or uncoordinated API design decisions among team members.	Mid	Duplicated dev effort, integration conflicts between frontend and backend, and missed sprint deliverables.	Hold brief regular standups, maintain clear task boards, and document API contracts before coding.	Conduct immediate alignment syncs to clarify task ownership and adjust broken interface contracts.
Framework & Tooling Inexperience – team members struggling with advanced framework concepts, database ORM patterns, or unfamiliar development tooling.	Low	Slower development velocity on complex features.	Conduct technical onboarding, establish starter code templates, and pair struggling developers with the technical lead or other developers.	Build internal time buffers into feature estimates and reassign complex technical tasks to more experienced members.
Data & Artifact Loss – accidental deletion of important data such as source code or database	Low	Lost development progress, time spent rewriting module code, and delayed sprint deliverables.	Enforce remote Git repository pushes daily, back up database migration scripts, and maintain cloud	Restore the latest working codebase and schema state from GitHub/cloud backups and recover lost progress.

Control & Monitoring

Control & Monitoring

- Project Tracker – indicate what will be the project tracker tools with the corresponding links.
- Code Management – indicate what will be the code repository tool and its link.
- Bug Tracking System – indicate how to track bugs. Indicated link when necessary.
- Daily Time Record – Indicate DTR Project Name

PROJECT TOOLS	
Project Management Tool / Project Tracker	1. Google Sheets 2. TFS (TBD)
Code Management	TFS (TBD)
Bug Tracking System	Google Sheets

Control & Monitoring

- Row may be added/removed depending on the project milestones / activities.


PROJECT TEMPLATES		
Document	Template (File Name)	Actual File (Naming Convention)
Meeting Minutes		
Review Minutes		
HLD		
LLD		
Document Review Checklist		
Unit Test Cases		
Unit Test Results		
Integration Test Cases		
Integration Test Results		
System Test Cases		
System Test Results		
Test Release Checklist		
Client Release Checklist		

Schedule

Project Schedule

Please refer to the WBS document.

Thank You!

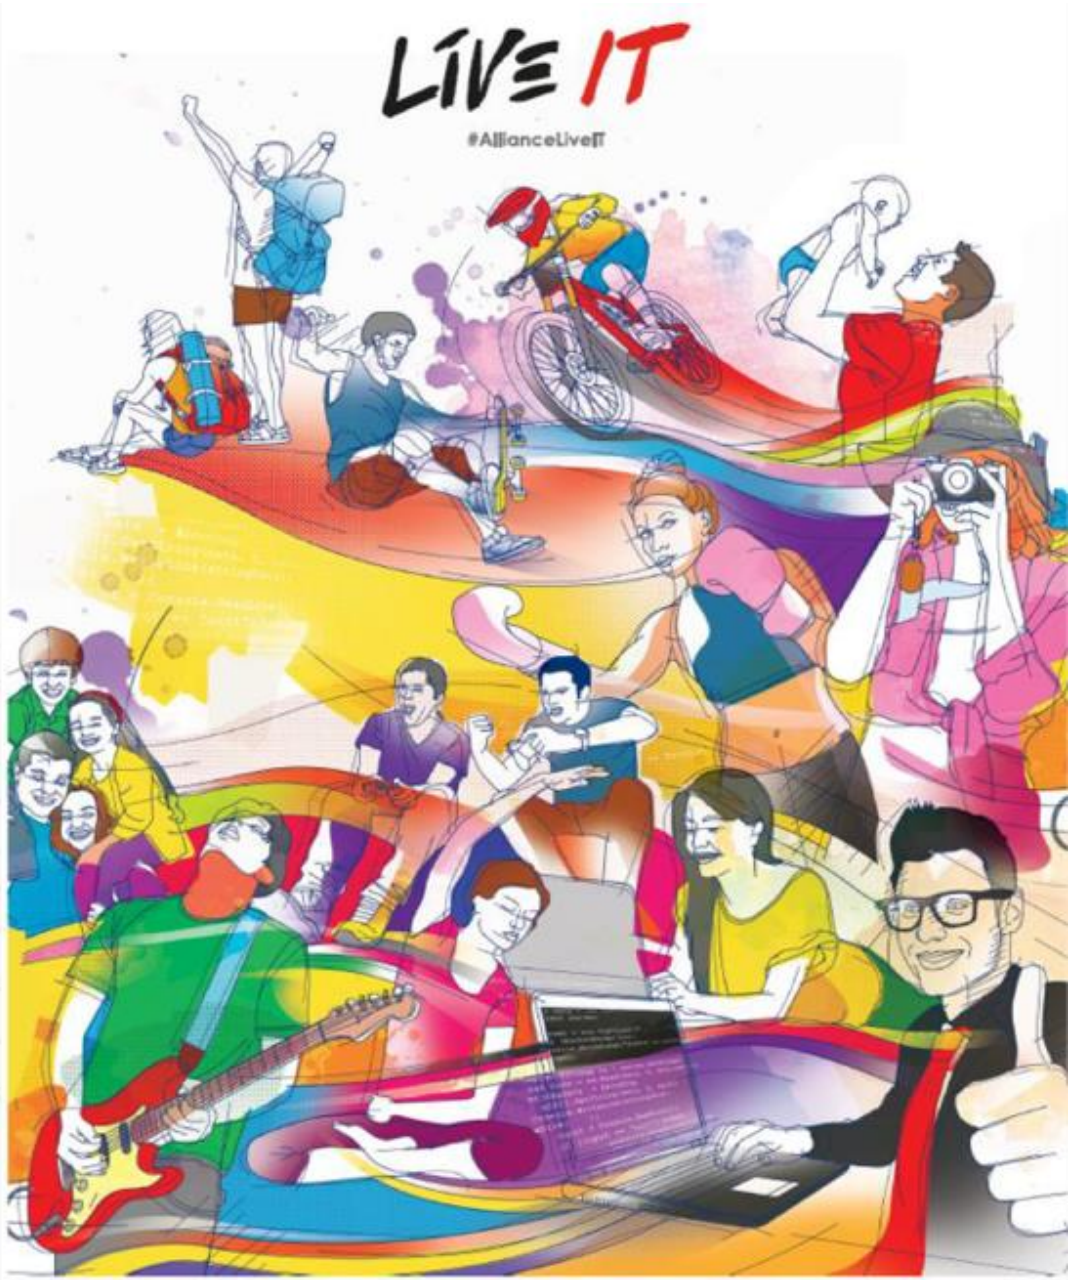

Alliance Software Incorporated

jobs@alliance.com.ph

+63 (032) 231 4219
238 6595

www.alliance.com.ph
